Testing Equipment Specialist Team Co.
Tel: +966 13 808 4277
Email: sales@testcosa.com
Aramco Report No:
Report No: TEST-143-34933-01

LIFTING EQUIPMENT INSPECTION REPORT	Area	Org. Code	Inspection Date	Inspection Time	Previous Sticker
	Jubail		**8th July 2025**	**10:00 AM**	No. **BV-24-4316** Issued By: **BUREAU VERITAS**
Department / Contractor	Equipment Number	Equipment Location		Inspection Reuslt	New Sticker No.
Sudhir Equipment Rental Co.	**S22SJ-1313**	**NAVAL BASE.**		**Pass**	**49081**
Manufacturer	Model	Capacity	Type	Eq. Serial Number	Sticker Expiration Date
JLG	**660SJ**	**250 KGS.**	**Boom Supported Elevating Work Platform (Manlift)**	**B300022023**	**7th January 2026**

Above Equipment was inspected by TEST in accordance with applicable Saudi Aramco GIs ASME API Standards. Deficiencies that require corrective action are listed below. Specific repairs to correct each dificiency should be noted in the corrective action taken column.

No.	Deficiencies	Correction Action Taken
1	Periodic Inspection, Visual and Functional Testing of Boom-Supported Elevating Work Platform (Manlift), As per SAGI.7.030 and ANSI A92.5, and it was Found Satisfactory at the time of the inspection. -Maintain PM. Service as per the Manufacturer's Recommendations.	

Receiver Name:	MD HASAN SARDAR	**Inspector Name:**	Kamel Mohamed
Signature:		**Signature:**	
Badge No.:		**CIU License No.:**	80019203
Telephone No.:	0545638024	**Telephone No:**	966581544944

When re-inspection is requested, a complete copy of this report should be ready to be reviewed by the inspector.

Distribution: Original - Porponent: 1st copy: TEST, 2nd copy: Inspector

Testing Equipment Specialist Team Co.
C.R. Number: 2050086551
Tel: +966 13 808 4277
Email: sales@testcosa.com

Inspection Checklist

Equipment Type:	Boom Supported Elevating Work Platform (Manlift)	Owner	Sudhir Equipment Rental Co.
Equipment No:	S22SJ-1313	Equipment Serial No.	B300022023
Aramco Report No:		TEST Report No.	TEST-143-34933-01

ID	ACCEPTANCE CRITERIA	REFERENCE	PASS	FAIL	N/A	REMARKS
1	**GENERAL REQUIREMENTS:**					
1.1	Equipment documentation is available	ANSI/SAIA A92.5, Sec: 4.16.1.1 G.I. 7.030	✓			
1.2	Previous inspection reports are checked	ANSI/SAIA A92.5, Sec: 5.11.1.3 G.I. 7.030	✓			
1.3	Daily pre-operational inspection checklists are checked (if applicable)	GI 7.030 Para: 5.1.2	✓			
1.4	Preventive Maintenance is established and updated records are maintained	ANSI/SAIA A92.5, Sec: 6.4.1	✓			
1.5	Equipment is operated by a qualified operator	ANSI/SAIA A92.5 Sec: 4.13.13	✓			
1.6	Warning notice, cautions or restrictions for safe operation and maintenance are clearly displayed and legible	ANSI/SAIA A92.5 Sec: 4.13.1	✓			
1.7	A sign is posted warning the operator not to rely solely on any automatic device as a substitute for safe operating practice	G.I. 7.030 Para: 5.6.2	✓			
1.8	Manufacturer name, address, serial number and model are clearly marked or tagged	ANSI/SAIA A92.5 Sec: 4.13.2	✓			
1.9	Safe working load and number of persons are clearly marked on the work platform	ANSI/SAIA A92.5, Sec: 4.13.3	✓			
1.10	Maximum platform height and reach are clearly marked	ANSI/SAIA A92.5 Sec: 4.13.4 & 5	✓			
1.11	Maximum travel height and travel directions are clearly marked	ANSI/SAIA A92.5 Sec: 4.13.9	✓			
1.12	Power rating are provided and marked (for AC and/or DC)	ANSI/SAIA A92.5 Sec: 4.13.6	✓			
1.13	Platform and guardrails electrical insulation data are provided	ANSI/SAIA A92.5 Sec: 4.13.10			✓	
2	**INSPECTION POINTS:**					
2.1	Platform surfaces are at least 18" (width & length) and are slip-resistant	ANSI/SAIA A92.5 4.12.1	✓			
2.2	Platform guardrails are provided and secure	ANSI/SAIA A92.5 4.12.2	✓			
2.3	Platform guardrails are 42" height (+/- 3")	ANSI/SAIA A92.5 Sec: 4.12.2.1	✓			
2.4	Platform toeboard is fitted and at least 4" high	ANSI/SAIA A92.5 Sec: 4.12.3	✓			
2.5	Moving parts are guarded	ANSI/SAIA A92.5 Sec: 4.11	✓			
2.6	Personnel on the platform is protected against the hazards of moving parts of the aerial platforms.	ANSI/SAIA A92.5 Sec: 7.10	✓			
2.7	Access to the platform is provided	ANSI/SAIA A92.5 Sec: 4.12.4	✓			
2.8	Access gates or openings shall be properly closed per the manufacturer’s instructions	ANSI/SAIA A92.5 Sec: 4.12.4	✓			

2.9	Electrical cables, wiring and components are undamaged	ANSI/SAIA A92.5 Sec:8.3	✓			
2.10	Safety harness anchorage is fitted in the platform	ANSI/SAIA A92.5 Sec: 4.12.5.1	✓			
2.11	Battery is secure, guarded and ventilated	ANSI/SAIA A92.5 Sec: 4.15.2	✓			
2.12	Outrigger position microswitches and interlocks are fully functional at their control panel	ANSI/SAIA A92.5 Sec: 4.7			✓	
2.13	Air, Hydraulic and fuel systems are not leaking	ANSI/SAIA A92.5 Sec: 6.6.5	✓			
2.14	Emergency stop button is available at ground control station	ANSI/SAIA A92.5 Sec: 4.6.3	✓			
2.15	There are no loose nuts, bolts, missing, worn or damaged parts around the structure	ANSI/SAIA A92.5 Sec: 6.6.2	✓			
2.16	The equipment is free of defective and/or corroded members/joints	ANSI/SAIA A92.5 Sec:6.4.3	✓			
2.17	Working environment is hazard free and machine can be safely operated	ANSI/SAIA A92.5 Sec:7.9	✓			
2.18	An hour meter is fitted	ANSI/SAIA A92.5 Sec:4.15.3	✓			
2.19	A fire extinguisher is fitted (type depends on operating location)	ANSI/SAIA A92.5 General	✓			
2.20	All moving parts are lubricated	ANSI/SAIA A92.5 Sec: 6.6.5	✓			
2.21	All fluid levels for oil, water and hydraulic are adequate	ANSI/SAIA A92.5 Sec: 6.6.5	✓			
2.22	Platform controls operate the machine correctly	ANSI/SAIA A92.5 Sec: 6.6.1	✓			
2.23	Platform controls are clearly marked with direction and mode of operation	ANSI/SAIA A92.5 Sec: 4.6.1.6	✓			
2.24	Platform controls accessible to the operator	ANSI/SAIA A92.5 Sec: 4.6.1.1	✓			
2.25	Platform controls return to "off" or "neutral" position when released	ANSI/SAIA A92.5 Sec: 4.6.1.4	✓			
2.26	Platform controls are protected against inadvertent operation	ANSI/SAIA A92.5 Sec: 1.3	✓			
2.27	Over-ride control for power functions is fitted at ground level control panel	ANSI/SAIA A92.5 Sec: 4.6.2.1	✓			
2.28	Lower controls return to "off" or "neutral" position when released	ANSI/SAIA A92.5 Sec: 4.6.2.4	✓			
2.29	Lower controls are clearly marked for direction and mode of operation	ANSI/SAIA A92.5 Sec: 4.6.2.6	✓			
2.30	Lower controls do not include drive and steering functions	ANSI/SAIA A92.5 Sec: 4.6.2.2	✓			
2.31	Lower controls are protected against inadvertent operation	ANSI/SAIA A92.5 Sec: 4.6.2.5	✓			
2.32	Boom raise/extend is operable from platform and ground control	ANSI/SAIA A92.5 Sec: 4.6.2.2	✓			
2.33	Boom lower/retract is operable from platform and ground control	ANSI/SAIA A92.5 Sec: 4.6.2.2	✓			
2.34	Platform rotation is operable from both platform and ground controls	ANSI/SAIA A92.5 Sec: 4.6.2.2	✓			
2.35	Emergency stop button is operable from both platform and ground controls	ANSI/SAIA A92.5 Sec: 4.6.3	✓			
2.36	Auxiliary/emergency lowering is operable from platform and ground controls	ANSI/SAIA A92.5 Sec: 4.6.4	✓			
2.37	Auxiliary/emergency retracting is operable from platform and ground controls	ANSI/SAIA A92.5 Sec: 4.6.4	✓			

2.38	Auxiliary/emergency rotating is operable from platform and ground controls	ANSI/SAIA A92.5 Sec: 4.6.4	✓			
2.39	Hydraulic/Pneumatic systems are leak-free with platform raised	ANSI/SAIA A92.5 Sec: 4.10.2	✓			
2.40	Tilt alarm is operable (5 degrees out of level) (manually depress the edge of the tilt switch to cause alarm condition)	ANSI/SAIA A92.5 Sec: 4.7.3	✓			
2.41	Aerial platforms is fitted with a warning device at the platform which activates automatically when the aerial platform is at and beyond the slope	ANSI/SAIA A92.5 Sec: 4.6.6	✓			
2.42	Tilt alarm is not combined with boom raise cut-out (dependent on machine manufacturer)	ANSI/SAIA A92.5 Sec: 4.6.6	✓			
2.43	Steering is properly working when moving forward and in reverse directions	ANSI/SAIA A92.5 Sec: 6.6.3.1	✓			
2.44	Brakes are in good working condition and can hold the machine on any slope (parking and moving)	ANSI/SAIA A92.5 Sec: 4.14.1	✓			
2.45	Extendable axles function is satisfactory (where fitted)	ANSI/SAIA A92.5 Sec: 7.3.3.8			✓	
2.46	Outriggers (stabilizers) extension-retraction operation is satisfactory	ANSI/SAIA A92.5 Sec: 7.10.3			✓	
2.47	Extendable elevating assembly operation is satisfactory (retracted vs. extended)	ANSI/SAIA A92.5 Sec: 4.2.1	✓			
2.48	Elevating assembly operation is satisfactory (elevated vs. lowered)	ANSI/SAIA A92.5 sec: 4.2.1(c)	✓			
2.49	Wheels and tires are serviceable and undamaged	ANSI/SAIA A92.5 Sec: 7.3.3 (6)	✓			
2.50	Travel alarm is operable	ANSI/SAIA A92.5 Sec: 6.6 (4)	✓			
2.51	Platform lowering alarm is operable	ANSI/SAIA A92.5 Sec: 6.6 (4)	✓			
2.52	Auxiliary power source available (to use in event of primary power loss)	ANSI/SAIA A92.5 Sec; 4.15.2	✓			
2.53	Platform does not descend when in raised position and the power is off	ANSI/SAIA A92.5 Sec: 4.6.3	✓			
2.54	Machine is safely drivable from the platform when raised (fast, slow, forward and reverse modes)	ANSI/SAIA A92.5 Sec: 6.6.3.1	✓			
2.55	The platform does not descend when in raised position and the power is off	ANSI/SAIA A92.5 Sec: 4.6.3	✓			
2.56	Engine powered machines fuel lines are supported to minimize chafing	ANSI/SAIA A92.5 Sec: 4.15.1	✓			
2.57	Engine powered machines fuel lines are positioned to minimize exposure to engine and exhaust heat	ANSI/SAIA A92.5 Sec: 4.15.1	✓			
2.58	Engine powered machines exhaust system is provided with muffler	ANSI/SAIA A92.5 Sec: 4.15.1	✓			
2.59	Installation of Anti- Entrapment device on work platform	Letter No. CIU-L-019/2016	✓			

Receiver Name:	MD HASAN SARDAR	**Inspector Name:**	Kamel Mohamed
Signature:		**Signature:**	
Badge No.:		**CIU License No.:**	80019203
Telephone No.:	0545638024	**Telephone No:**	966581544944

Testing Equipment Specialist Team Co.
C.R. Number: 2050086551
Tel: +966 13 808 4277
Email: sales@testcosa.com

ATTACHED PHOTOS

Equipment Type:	Boom Supported Elevating Work Platform (Manlift)	Owner	Sudhir Equipment Rental Co.
Equipment No:	S22SJ-1313	Equipment Serial No.	B300022023
Aramco Report No:		TEST Report No.	TEST-143-34933-01

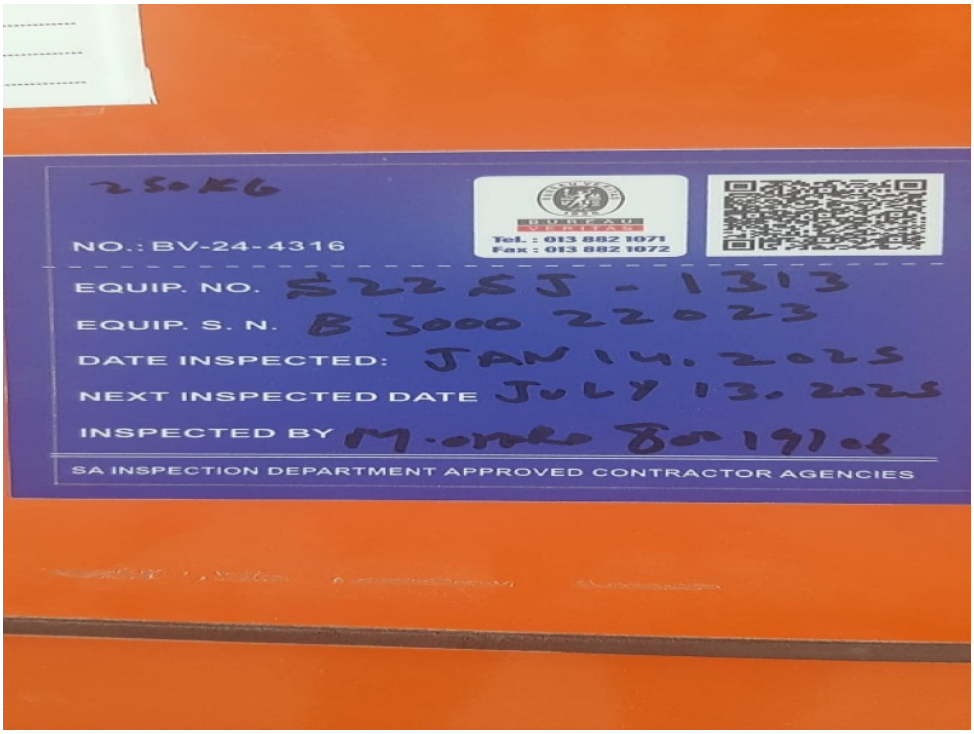

TEST®

Testing Equipment Specialist Team

Sticker No:	**49081**
Equipment No:	S22SJ-1313
Equipment SN:	B300022023
Date Inspected:	8th July 2025 10:00 AM
Next Inspection Date:	7th January 2026
Inspected By:	Kamel Mohamed (80019203)

SA INSPECTION DEPT. APPROVED CONTRACTOR AGENCY

TESTING EQUIPMENT SPECIALIST TEAM Co.

Tel: (013) 808 4277 - Mob: 0533074795 - Email: SALES@TESTCOSA.COM
